
## Aldrich Park Trail Final Report

**Andrew Pearl** 

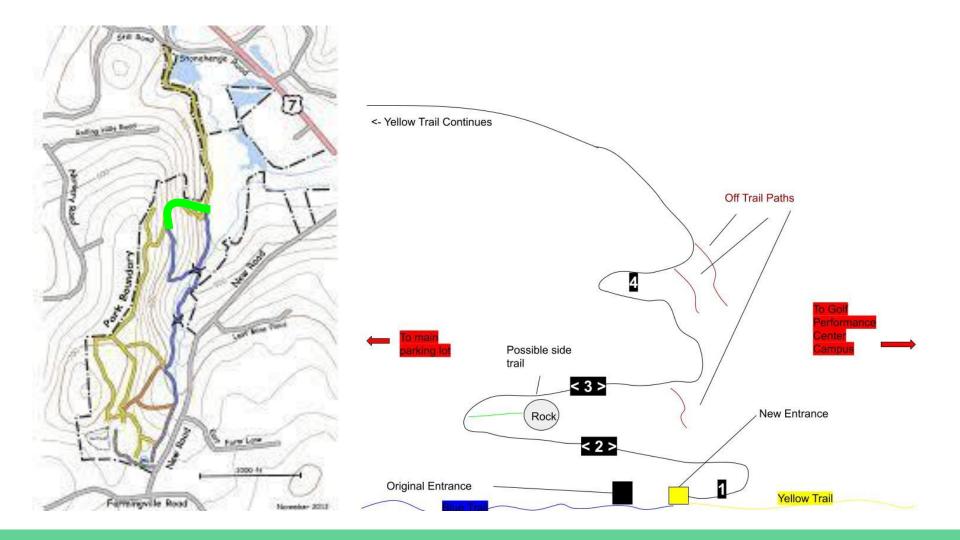

## **Project Timeline**

6/5: Initial Presentation at Conservation Commission

**6/19**: Tools instruction session with Mr. Sharp and Mr. Liptack

7/15: Work session 1 - leveled out more than half of trail, raked out rest of trail.

**8/13**: Work session 2 - finished clearing trail, began refining rock retaining walls, began covering up old trail.

**9/9**: Work session 3 - Blazed new trail, covered old blazes, finished retaining walls, chopped roots, filled holes, finished covering up old trail.

11/27: Final Presentation at Conservation Commission

## Key Changes















### Leadership/Organization

#### **Success**

- -Bringing scouts together
- -Seeing enjoyment/pride
- -Delegating efficiently





#### **Challenges**

- -Recruiting enough volunteers midsummer
- -Maintaining safety
- -Giving positive feedback/motivation

#### Cost/Hours

Estimated Cost: \$130 Hours

Actual Cost: \$105 Myself: 19

\$68 for refreshments Scout help: 47

\$37 for paint Adult help: 12

78 Total Hours

# Thank You

Conservation Commission, Mr. Sharp, Mr. Liptack, Mr. Gary Holland, Scout/Parent Volunteers, The Pearl Family
